



PHASE 1 DEMO (SEP 2019 - FEB 2020)


- General Notes:**
- Construction Fence will be installed on the limits of work line with the exception of locations that have Sound Wall. Fencing will be modified as required to accommodate phasing.
 - Porter Kresge Road is 16' Wide. One line will remain open at all times. All delivery vehicles must not be wider than 8' unless authorized by Swinerton's Superintendent.
 - Contractor Parking will start just north of the jobsite. Parking will be in one lane of Porter Kresge Road all the way to Heller Road. The other will be utilized for emergency access.
 - Work Hours will be from 7:00AM to 3:30PM Monday through Friday. No noisy work will occur before 8:00AM in the morning.
 - All material/equipment must be put in place within 24 hours (just in time). No storage of materials or equipment will be authorized on site. Exceptions must be authorized by Swinerton's Superintendent.
 - All non-construction personal will utilize the Turn-Around area shown and will not be allowed to drive through the construction zone.
 - Sound Wall will be placed 5' away for existing structure and to a height that is just above the top window of the Sensitive Occupied Structure.
 - The Backyard Area (near the laydown area) will be utilized as a lunch and break area during Phase 1, 2, and 3 work.




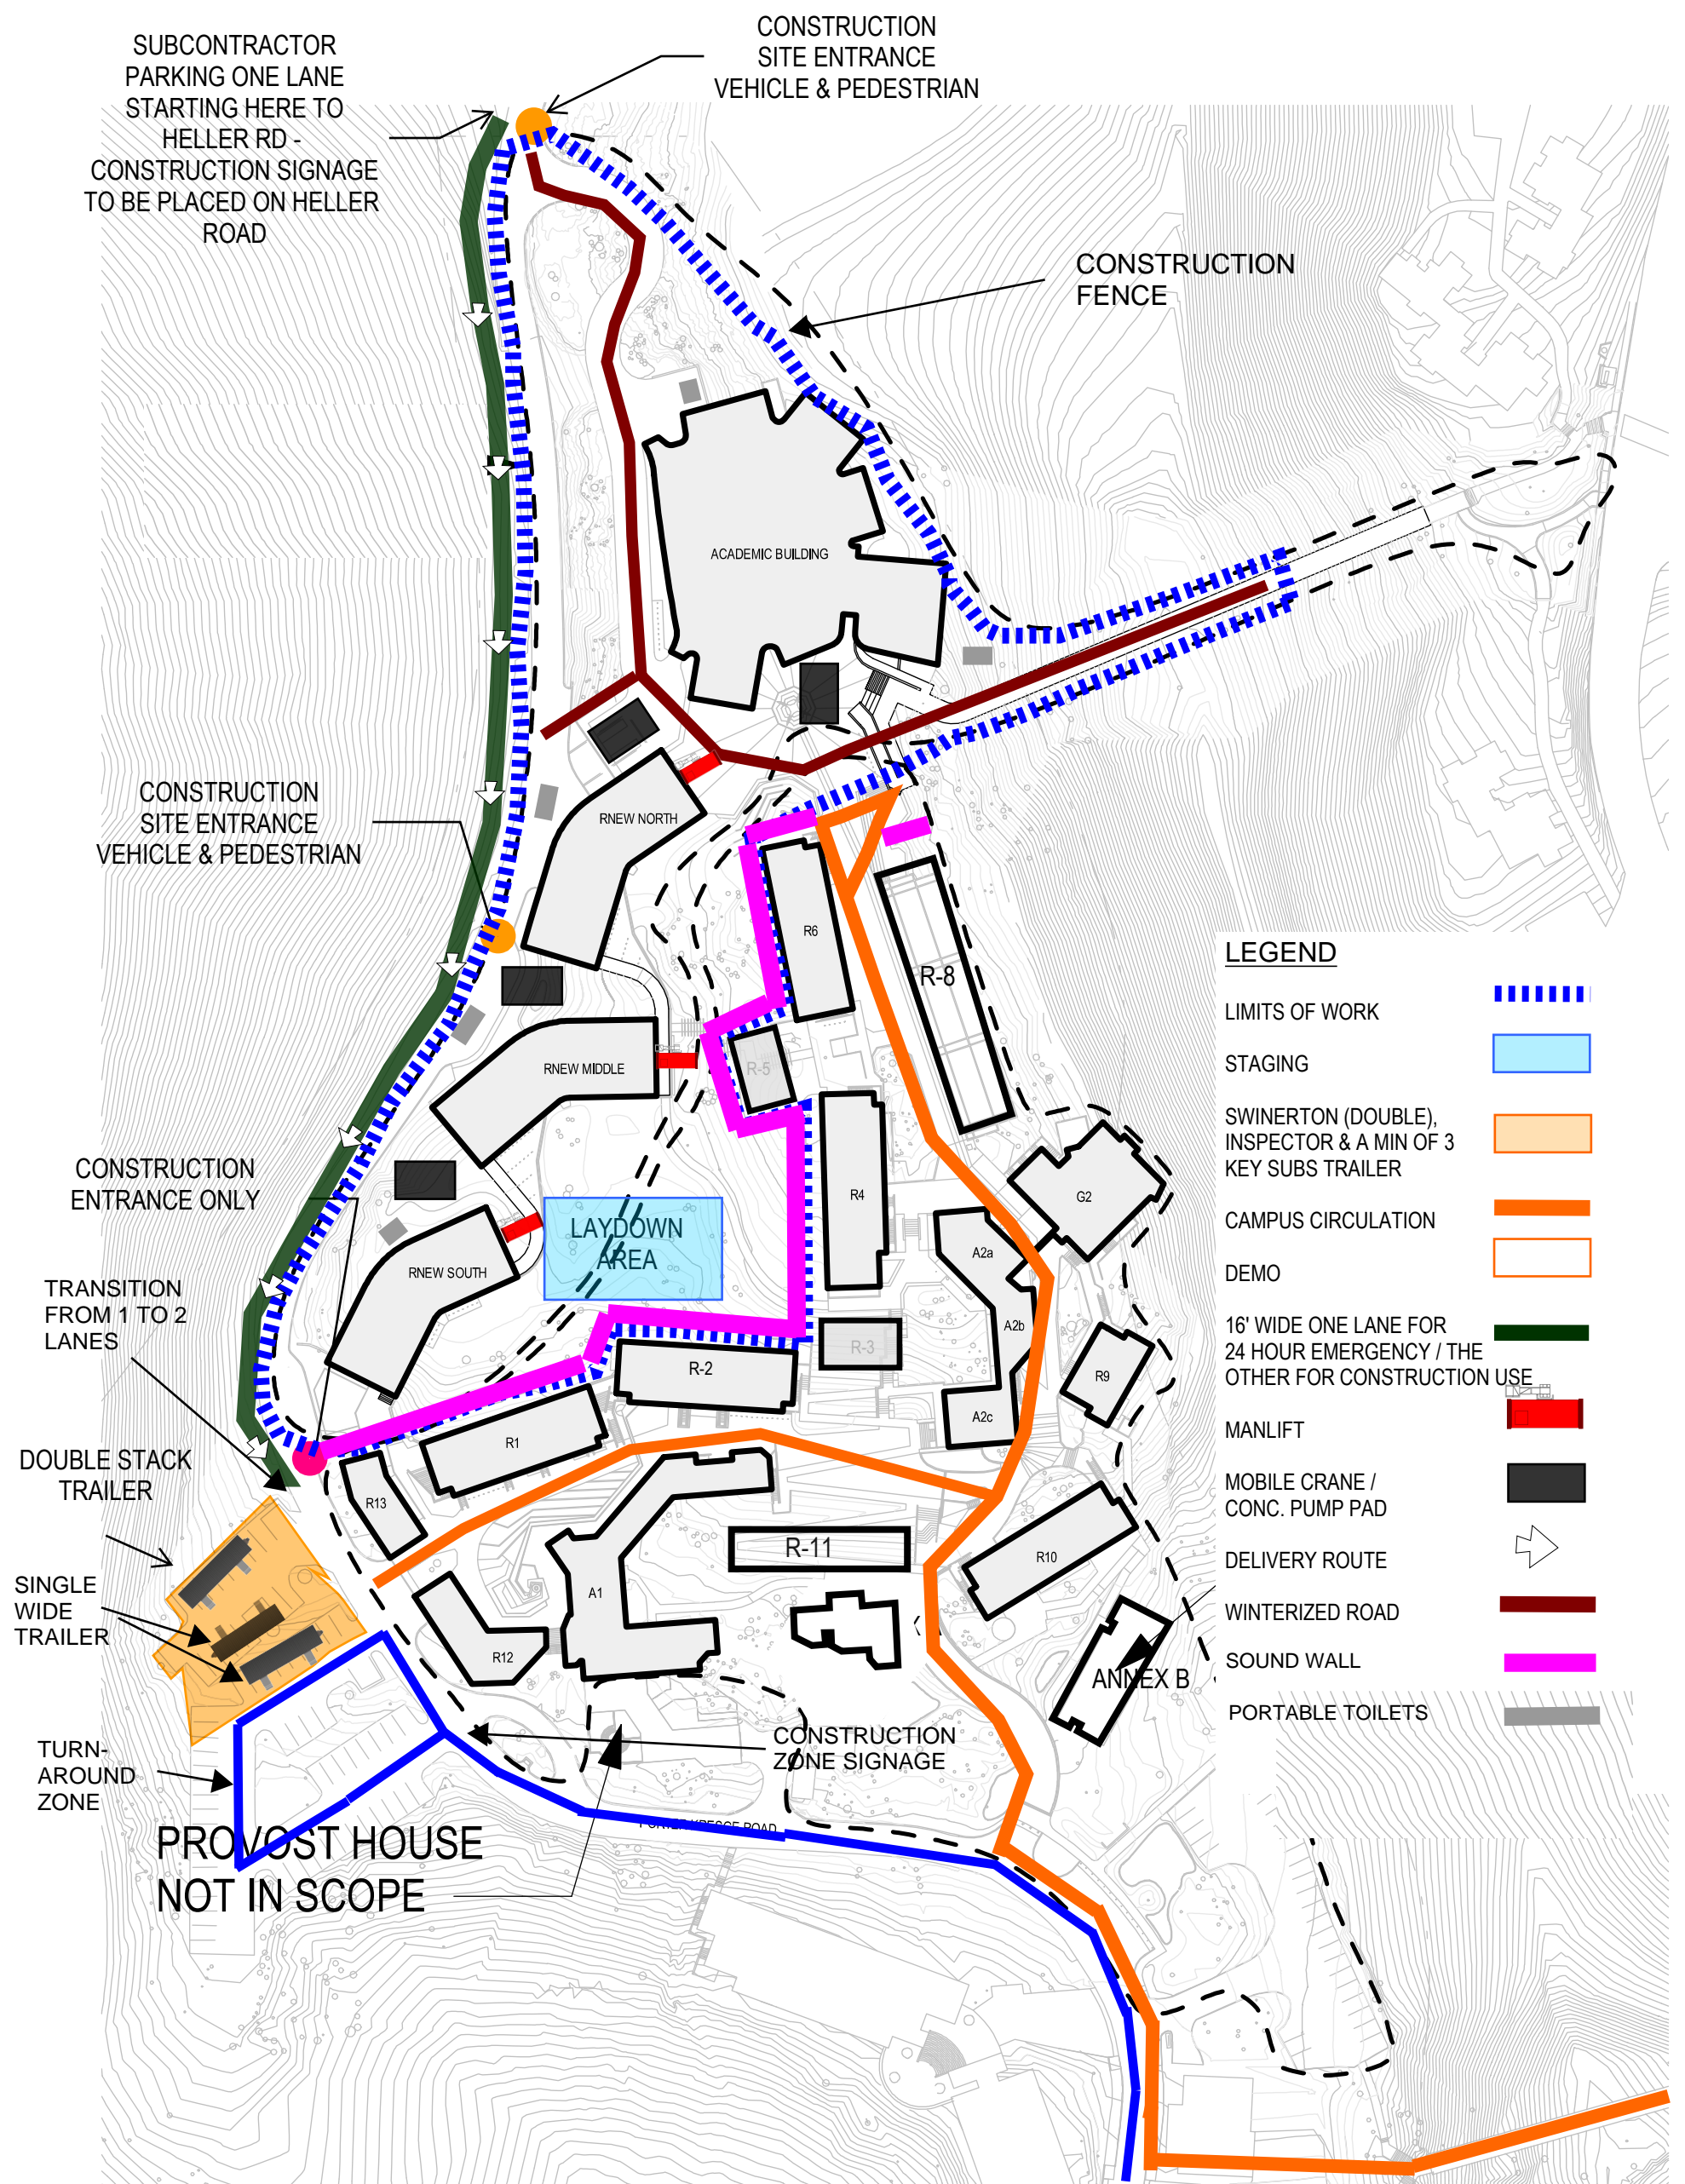

PHASE 2 RNEW & ACAD CONSTRUCTION

RNEW SOUTH - 1/23/20 TO 3/31/21 W/O WEATHER
RNEW MIDDLE - 2/11/20 TO 4/06/21 W/O WEATHER
RNEW NORTH - 3/23/20 TO 6/30/21 W/O WEATHER
ACAD - 2/24/20 TO 6/10/21 W/O WEATHER
BRIDGE - 7/17/20 TO 2/08/21 W/O WEATHER



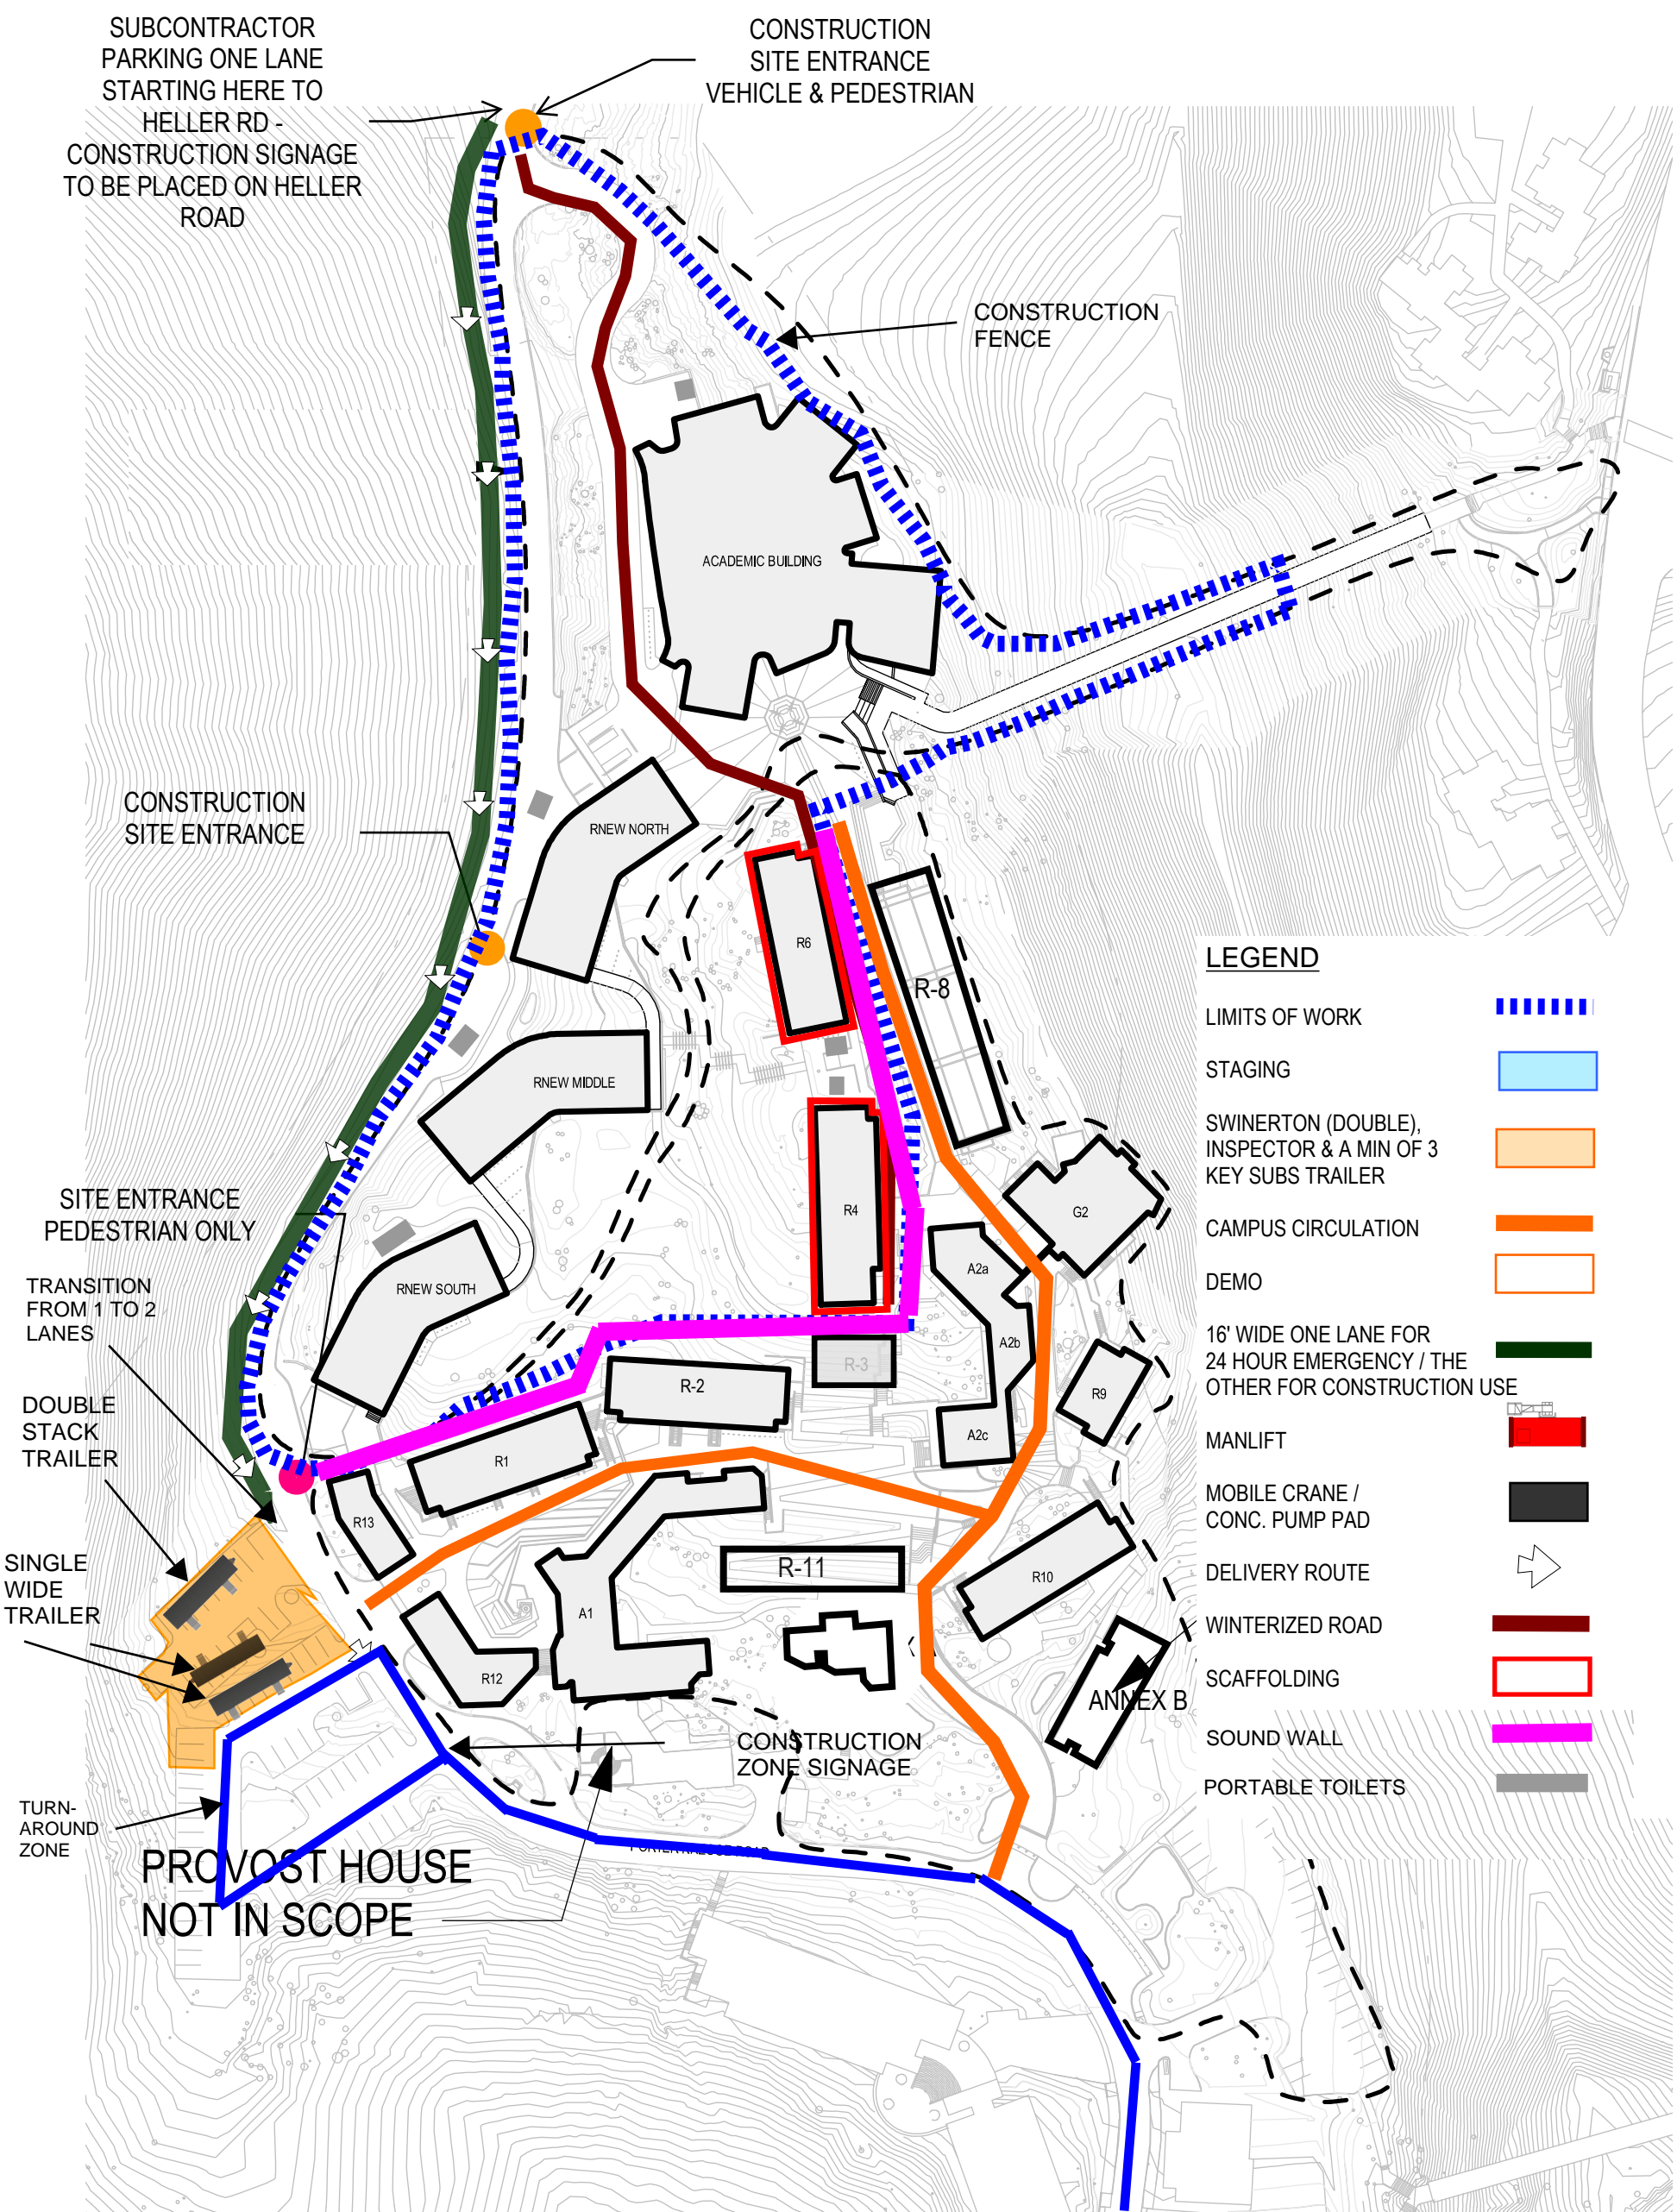

PHASE 3 RNEW, ACAD, R4 & R6 CONSTRUCTION

R5 - 8/17/20 TO 9/14/20 W/O WEATHER
R6- 8/19/20 TO 4/9/21 W/O WEATHER
R4- 8/3/20 TO 4/9/21 W/O WEATHER

